



Implementation Update on  
SPDA  
Special Program for the Development of Africa



COMCEC, 38<sup>th</sup> Ministerial Session  
26-29 November 2022  
November 2022



## Contents

I.	Introduction.....	1
II.	What was committed.....	1
III.	What was Approved .....	2
IV.	What was expected - Expected Outputs.....	2
V.	Implementation Status .....	3
VI.	Some of the Key achievements of the Program.....	7
2.1	Project- specific achievements .....	7
	Roseires Dam in Sudan .....	7
	Basic Urban Infrastructure for Social Housing Project in Bamako, Mali .....	7
	Support to Social Housing Project in Bamako, Mali .....	8
	Linguere-Matam Road - Senegal.....	8
	Construction of the Dapaong-Ponio- Border Road, Burkina Faso.....	8
	Construction of Koudougou Dedougou Road Project, Burkina Faso .....	8
	Construction of Bassar- Katchamba Road Project, (Guerin Kouka - Katchamba Road section, 26 km),Togo .....	9
	Support to the Post-Conflict Reconstruction Programme for the Centre-North-West in Cote d'Ivoire. ....	9
2.2	<i>Some of the overall achievements</i> .....	10
VII	Conclusion .....	11
	Annex 1: Active, Complete and Terminated IsDB Interventions under SPDA .....	12
	Annex 2: List of Approvals .....	12

## I. Introduction

1. The Third Extraordinary Summit of the OIC held in Makkah, Saudi Arabia in December 2005, recommended the formulation of “a special program for the development of Africa” to tackle poverty, build capacity, eliminate illiteracy, and eradicate diseases and epidemics in member countries in Africa. In this regard, the Special Program for the Development of Africa (SPDA) was formulated and launched after its validation at a Ministerial Meeting held in Dakar, Senegal, in January 2008. It succeeded a similar program, the IsDB Cooperation Framework for Africa (Ouagadougou Declaration) implemented by the Islamic Development Bank for Sub Saharan African (SSA) countries from 2003 to 2007.
2. In formulating the SPDA, consultations were held with African member countries to take on board their aspirations and priority needs and, at the same time, instill identification with, and ownership of the program. The consultations resulted in the identification of the overall objective of the program as that of poverty reduction (in the context of attainment of the MDGs and trade promotion). The former is achievable through appropriate investments in Agriculture, Water and Sanitation, Education, Health, Energy and Infrastructure. By focusing on infrastructure, agriculture, and energy, the SPDA was aimed at easing the binding constraints in these sectors and to spur economic growth, reinvigorate agricultural production and create employment opportunities – all being the key enablers of poverty reduction. A trade promotion objective involves supporting African member countries to increase regional and international trade by exploiting the trade opportunities that OIC membership brings was also a part of the program.
3. SPDA benefitted 22 African countries namely: Benin, Burkina Faso, Cameroon, Chad, Comoros, Côte d'Ivoire, Djibouti, Gabon, The Gambia, Guinea, Guinea Bissau, Mali, Mauritania, Mozambique, Niger, Nigeria, Senegal, Sierra Leone, Somalia, The Sudan, Togo and Uganda.
4. Since the end of the approval phase of the SPDA in November 2012, the focus has been on deepening the implementation of 480 operations approved for the member countries to ensure that the expected outputs are delivered and expected outcomes achieved.
5. This is an update on its implementation since then and some of the achievements so far.

## II. What was committed

6. The IsDB Group earmarked US\$4.0 billion over the five-year period (1429H-1433H/2008-2012), twice the amount devoted to the Ouagadougou Declaration to implement the SPDA. The program was supported by all the entities of IsDB Group: The IsDB itself, which provides ordinary financing; the Islamic Solidarity Fund for Development (ISFD); the trade financing entity (International Islamic Trade Finance Corporation, ITFC) and the private sector window of the IsDB Group (Islamic Corporation for the Development of the Private Sector ICD). Islamic insurance was offered by ICIEC while capacity building in Islamic Finance was provided by IRTI, currently the IsDB Institute.

7. About 37 percent or US\$1.5 billion of the total financing was pledged from IsDB's ordinary resources, while 33 percent (US\$1.3 billion) from the ISFD; a further 27percent (US\$ 1.1 million) for trade operations by ITFC, and three percent (US\$ 0.12 million) for private sector development by ICD. ICIEC had no specific allocation, instead it provided insurance cover to ITFC and ICD operations. The Group-wide financing plan is shown in Table1.

**Table 1 IDB Group Annual Financing Plan (1429-1433H) (US\$ M)**

Window/Year	1429H	1430H	1431H	1432H	1433H	Total
	2008	2009	2010	2011	2012	(US\$)
Ordinary Operations (ISFD included)	420	481	550	630	720	2,800
Trade Operations - ITFC	160	183	210	240	274	1,067
Private Sector Development (ICD)	20	23	26	30	34	133
<b>Total (US\$)</b>	<b>600</b>	<b>687</b>	<b>786</b>	<b>899</b>	<b>1,029</b>	<b>4,000</b>

Source: SPDA Framework for Action 1429 H/2008G/IDB

8. The SPDA approval phase ended in November 2012 (end of 1433H) and since then, the focus has been on deepening the implementation phase as about US\$ 1.7 billion of the OCR financing of US\$ 3.7 billion were approved in the last two years of the Program.

### III. What was Approved

9. By the end of the program in 1433H (12 November 2012), total approvals by the IsDB Group amounted to US\$5.01 billion for 480 operations (project financing, trade and Waqf operations). These approvals represented an "achievement rate" of 125 percent of the earmarked allocations

**Table 2 - Gross Approvals for SPDA (1429H-1433H)<sup>1</sup> (USD Millions)**

	1429 2008	1430 2009	1431 2010	1432 2011	1433 2012	Total
OCR Project Financing	537.4	577.6	788.7	870.4	875.3	3,649.3
Other Project Financing (UIF, APIF, Treasury)	93.5	14.3	94.3	43.4	40.8	286.2
Private Sector Development - ICD project Financing	75.5	9.3	42.0	43.4	28.0	198.1
Trade Financing (ITFC, UIF)	317.6	129.5	212.2	179.9	226.9	1,066.0
of which ITFC	310.1	119.5	212.2	175.9	217.9	1,035.5
Waqf Fund Financing	0.8	1.1	0.8	2.7	0.0	5.3
<b>Total</b>	<b>949.2</b>	<b>722.5</b>	<b>1,095.9</b>	<b>1,096.3</b>	<b>1,142.9</b>	<b>5,006.9</b>

Source: SPDA Comcec Update, 2018

### IV. What was expected - Expected Outputs

10. This section takes a glimpse of the projects that have been approved for SPDA to show some of the expected outputs when these projects are fully and effectively implemented.

11. For **infrastructure**, a combined total of over 2,500 KM of roads will have been either constructed or upgraded in 13-member countries. This is in addition to two new airports that have been approved for Senegal and Sudan to enhance these economies and strengthen their role as sub-regional air hubs. More than 900MW of electricity will be

produced in six countries mainly from hydroelectric sources, further strengthening the environmental sustainability of the region. This will involve the laying of almost 700 KM of power lines and will result in over 40,000 households having increased access to energy. Taking the average household size of six, this translates to about a quarter million people with increased access to energy. Streetlights, amounting to about 800, will also be built in 2 countries. Through the ECOWAN project, Gambia and Sierra Leone will see their broadband subscriptions increase 13-fold, while the number of internet users will increase 6-fold, and about 1,500 KM of fiber optic cable laid. Support to water and sanitation will result in water distribution increasing to cover an area of 800 square km, bringing over 200,000 cubic meters of water a day to the populations. This translates to over 50,000 households having access to clean water and reservoirs with capacities of 45,000 cubic meters a day built.

12. With respect to **education**, by the end of the implementation phase of SPDA, more than 325 new primary and secondary schools and over 1,000 classrooms would have been built and equipped. This will be in addition to three technical colleges and eight university faculties also built or equipped. Since increased access to education must be complemented by increased quality, approvals have been made to enhance the capacity of teachers, teaching inspectors, administrators and lecturers in seven countries in addition to the provision of teaching materials. To help address youth unemployment and improve the quality of education, over 400 new classrooms in 120 new madrassas serving over 5000 students, mainly girls and students from poor backgrounds, will be built in Niger, Gambia, Senegal, and Nigeria.
13. In the **health** sector, over 10 new hospitals and over 120 clinics, health centers and Primary Health Care Centers would have been built or upgraded as a result of the full implementation of the SPDA. This would result in an increase in bed- capacity in these institutions by about 1,200. Alongside this, almost a million Long Lasting Insecticidal Nets (LLINs) would have been provided to combat malaria. To strengthen the capacity for improved health care delivery, over 20 medical doctors and over 500 cardiology students, Medical Technicians and Ophthalmologists would have been trained. In addition, medical equipment for cardiology and surgical centers as well as medical laboratories would have been provided.
14. With respect to **agriculture**, over 800,000 hectares of land would have been developed and cultivated including marginal lands in some member countries. This is expected to result in increased production of staple and cash crops. Additionally, 8-10 strategic grain reserves would have been built to smooth out consumption given the vulnerability of some member countries to food insecurity arising from either floods or droughts. To encourage agricultural research, 5-6 soil and or seed research laboratories would have been built, refurbished, or upgraded by the end after full implementation of the SPDA.

## **V. Implementation Status**

### **a. Completed projects**


15. More than 280 projects/ grants were approved by the IsDB during the approval phase of the SPDA, including 124 grants and 139 and 156 projects. As of October 31, 2022, 82 projects and 123 grants have been completed and fully disbursed (50% of approvals), 3 projects have been terminated after disbursing 2/3 of the approved amounts, 54 projects and 1 grant are still active, and 17 projects have been cancelled (10% of the IsDB approvals). (see Annex 1).

16. Representing the lion's share in terms of interventions, the completed projects/grants benefited all 22 countries covered by the program, with Mauritania, Senegal, Chad, Sudan, and Mali being the top 5 beneficiary countries. (See Table 3 for details)

Table 3: Completed IsDB Interventions by Country

Country	Grants			Projects			Cumulative		
	#Grants	Approvals (\$m)	Disbursements (\$m)	#Projects	Appr\$m	Disbursements (\$m)	Total Projects	Total Appr (\$m)	Total Disbursements (\$m)
Mauritania	7	2	2	11	299	299	18	301	301
Senegal	4	2	2	8	286	286	12	288	288
Chad	6	1	1	6	175	175	12	176	176
Sudan	9	2	2	7	148	148	16	150	150
Mali	8	3	3	7	127	127	15	130	130
Gabon				1	77	77	1	77	77
Uganda	6	1	1	5	69	69	11	70	70
Nigeria	7	1	1	1	63	63	8	64	64
Benin	6	1	1	4	60	60	10	62	62
Gambia	5	1	1	5	56	56	10	57	57
Sierra Leone	2	1	1	3	55	55	5	56	56
Cote d'Ivoire				3	56	56	3	56	56
Togo	2	1	1	4	46	46	6	47	47
Burkina Faso	9	2	2	4	44	44	13	46	46
Djibouti	5	1	1	5	45	45	10	46	46
Guinea	3	1	1	3	38	38	6	39	39
Mozambique	5	2	2	3	36	36	8	38	38
Niger	11	4	4	1	30	30	12	34	34
Somalia	14	8	8				14	8	8
Cameroon	4	1	1	1	6	6	5	7	7
Comoros	8	3	3				8	3	3
Guinea-Bissa	2	1	1				2	1	1
<b>Grand Total</b>	<b>123</b>	<b>37</b>	<b>37</b>	<b>82</b>	<b>1,715</b>	<b>1,715</b>	<b>205</b>	<b>1,753</b>	<b>1,753</b>

17. With respect to the sectoral financing under OCR, more than two third of the funds (70%) went to the economics sectors of transportation (34%), agriculture (17%), energy (12%), industry & mining (7%), followed by human capital at 17%. These investments in socio-economic infrastructures are essential in creating an enabling environment for sustainable development.

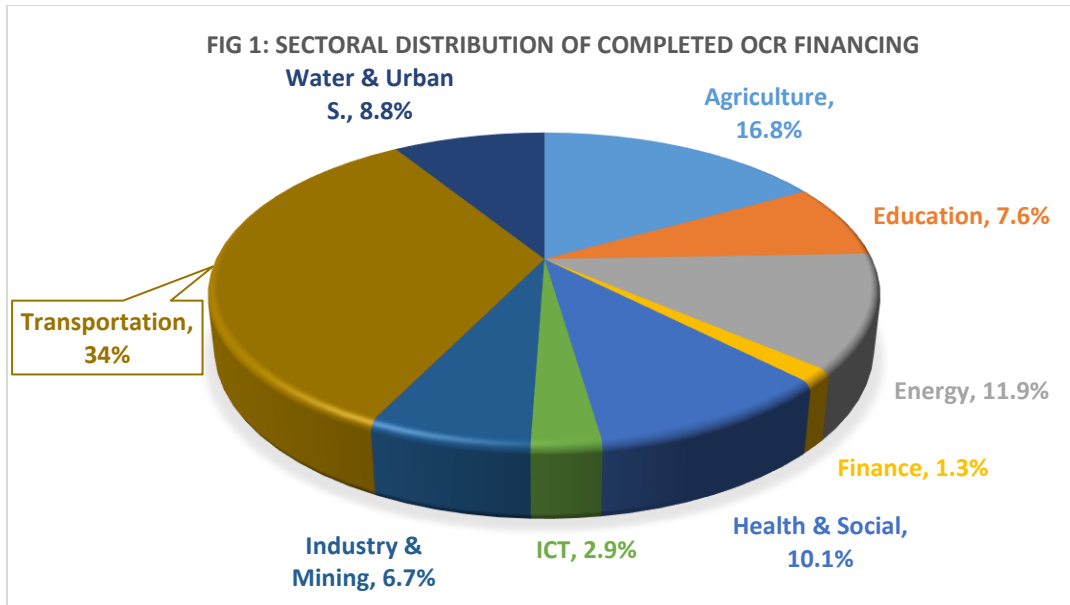

18. In terms of number of completed operations, grants were the majority (62%) while non-grants operations represent 38% in the form of Loans, Istisnaa, etc.

**b. Active projects**


19. The size and structure of the active portfolio shows that the program is close to completion. As of October 31, 54 projects and one grant are still active. The objective of this ISFD grant approved in 2012 [Dryland Development Project (EARDP Initiative)] was to contribute to the strategy of the Government of Somalia to restore basic social services and rebuild livelihood assets of the pastoralists and semi-pastoralists. The grant is 86% disbursed and is ready for closure.

20. Eight of the 54 projects are ready for closure. This active portfolio has disbursed US\$ 926 million of the 54 projects (more than 2/3 of the approvals), with only US\$131 million in uncommitted funds representing 10% of the current active portfolio and less than 5% of the total approvals.

21. Most of these interventions are in the sector of agriculture (44%), followed by water and urban services at 18% and transportation at 16%. (See figure 2 for details).

Figure 2: Sector financing – Active projects (In US\$)



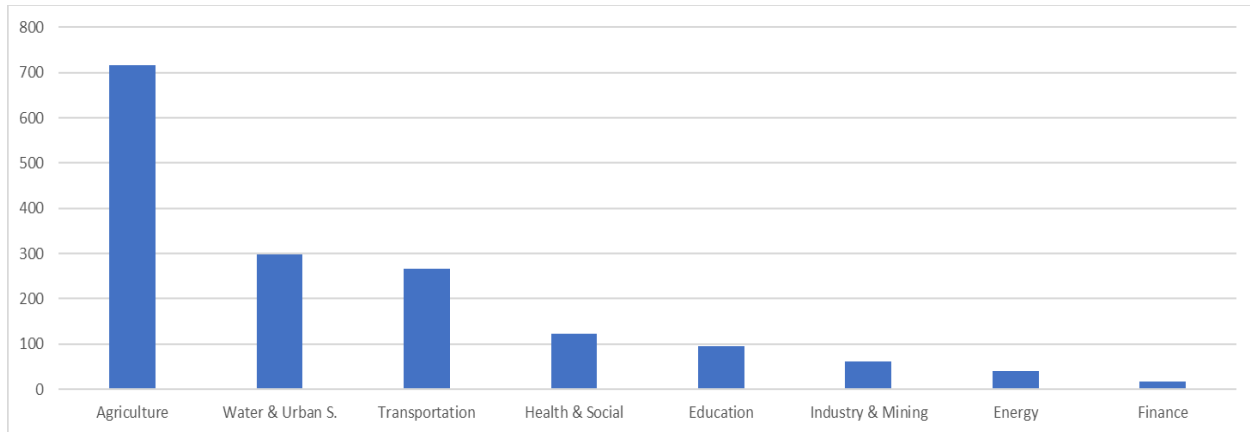

### c. Cancelled projects

22. Across the IsDB Group, only 32 operations/projects, valued at USD 477, have been cancelled, representing 9.2% of the gross approvals. In terms of OCR financing, 17 projects, were cancelled in 11 countries as indicated in table 4 below. Most of the cancelled projects are in agriculture, health, and infrastructure. The largest project cancelled is the Khartoum new International Airport in Sudan, approved for US\$150 million, followed by the 70-megawatt power plant in Senegal, approved for US\$ 97 million.

Table 4: OCR Cancellation by country

Region Of Hub	Country	Project Code	Projects	Sum of Appr. (\$m)
Regional Hub	Mozambique	MOZ0034	Preparation Facility for the ISFD Sustainable	0.09
	Somalia	SOM0080	Emergency Services / Supplies	0.2
	Uganda	UGA0063	Replenishment of food security stocks- Phase I Jeddah Declaration	0.5
RH - Abuja	Niger	NER0098	Malaria prevention and Control	5.19
	Nigeria	NGA0055	Nigeria Emergency Management Agency (NEMA)	0.25
RH - Cairo	Sudan	SDN0154	Khartoum New Int'l Airport	150
		SDN0162	Wamy Sudan Residential & Commercial Building	8
		SDN0163	Munazzamat Addawa Al Islami	10
		SDN0165	Sudan Consulate & Hajj Mission Building	15
RH - Dakar	Cote d'Ivoire	CIV0502	Purchase of medicine for refugees of (ZR) in Congo E	0.1
	Guinea-Bissau	GNB0033	Design Implementation of Food Security (JED. Declar	2
	Mali	MLI0095	Pilot Program on Roll Back Malaria (Quick Win)	5.32
		MLI0110	Markala Sugar Project	40.47
		MLI0941	Kayes-Diamou-Bafoulabe Road	8
Senegal	SEN0121	70 Mega Watt Power Plant	95.51	
RH - Rabat	Mauritania	MRT0119	Irrigation Development Project in R'KIZ Eastern Bassin	12.84
		MRT0148	Support to Expansion of Health Coverage in Rural Areas	15.88
<b>Grand Total</b>				<b>369.35</b>

## VI. Some of the Key achievements of the Program

In this section we present some of the achievements so far. They are extracted from completed projects with the full Project Completion Report (PCR) completed. Hence, other projects that are completed but their PCRS are not yet finalized yet, are not included in these lists. The achievements are categorized into two – the first looks at project-specific achievements across the region, while the second accumulates the achievements (see Table 1).

### 2.1 Project- specific achievements

A summary on eight completed projects is given below.

#### Roseires Dam in Sudan

This project heightened the Roseires Dam in Sudan by ten meters and increased the reservoir capacity by four billion cubic meters of water (from 3 to 7.4 billion cubic meters) to irrigate about one million hectares of fertile land downstream. An additional 30,000 hectares of land resulting from filling and emptying of the Reservoir was created. The opportunity of increased cultivation by farmers and increased acreage of irrigable land for local and foreign investment for food security have resulted from this project. In addition, the Project increased the generated hydropower from 1200GWh/year to 1800GWh/year annually, which did not entail any additional investment in the turbines or other electromechanical equipment or transmission lines. Furthermore, a housing compounds project consisting of 22,000 houses, with service utilities, distributed in 12 towns on both eastern and western banks were also built to relocate and compensate the people affected by the project.

IsDB co-financed the project with AFESD and OFID by contributing USD 80 million (17% of the total cost).

#### Basic Urban Infrastructure for Social Housing Project in Bamako, Mali

Aimed at contributing to poverty alleviation and reduction of economic disparities in Bamako by providing decent and affordable properties with all the basic services and functionalities installed, the project provides increased access to decent low-cost housing and basic social infrastructure to a large number of low and middle incomes households.

The project led to the construction of 1,492 Houses (all connected to the sewerage system, the piped water supply and the electricity grid network); 4.4 km of main roads constructed with bitumen within the new district; 15.4 km of secondary roads (with laterite); and 44.8 km of surface water drainage network.

The project was approved in June 2011 and completed in 2015.

### Support to Social Housing Project in Bamako, Mali

Encouraged by the positive response to the Bamako social housing project, IsDB co-financed this project that resulted in the construction of 1,000 houses, of which 500 houses were financed by IsDB. Other components of the project include 1.7 km of bituminized main roads and 11.8 km of secondary laterite roads and 13.2 km of surface water drainage. All the 1,000 households have access to a sewer system as well as the water and electricity networks. In addition, streets lighting, and crossroads are provided.

The project was approved in February 2012 and completed in December 2014.

### Linguere-Matam Road - Senegal

This is a 55km section of the Linguere-Matam road between Boula – Patouki, which is contributing to the efficient movement of freight and passenger traffic in Northern Senegal. The project generated increased use of transport services by area residents and enhanced their access to social services and job opportunities, saving traveling time by about 3 hours and reducing vehicle operating cost by at least 50%. During implementation, some activities were added to deepen the project's development impact. These are a 660-m long access road to Ranerou Center and a 10000m<sup>2</sup> park.

### Construction of the Dapaong-Ponio- Border Road, Burkina Faso

The project resulted in the construction of 38 Km of road to increase accessibility in northern Togo and facilitate movement goods and people with neighboring countries of Niger and Burkina Faso. Other components include drainage facilities, four bridges at Tamgbamonte, Nadougou, Tambouaga and Ponio, control signs, a toll post, information panel and pavements marking. Aside from the other benefits including reduction in travel time and transportation costs, and easy access to health and educational facilities, the project has resulted in an increase of the traffic between Lomé and Niamey.

### Construction of Koudougou Dedougou Road Project, Burkina Faso

This project resulted in upgrading an existing earth road to an all-weather road of 130 Km linking Koudougou to Dedougou in Northern Burkina Faso thereby easing movement of goods and services with neighboring countries. It resulted in widening the rural road, construction of 3 concrete bridges, 2 toll payment stations, 4 boreholes, 13,500m of fences, 35km of access roads and a few trees.

This project is resulting in, among other things, the reduction of vehicles operating costs and travel time while promoting economic growth and poverty reduction. The project supported the government's strategy of improving national and international transport links to foster trade and economic growth.

### Construction of Bassar- Katchamba Road Project, (Guerin Kouka - Katchamba Road section, 26 km),Togo

The main objective of the project is to encourage the economic and social development of the remote western agricultural areas of the regions of Kara and Savanes through the upgrading and surfacing of an existing earth road linking Guerin Kouka to Katchamba. Overall, 27.2 km (21 km of main road section and 6.2km of Katchamba road access) of paved road was built and in addition, 5 schools were rehabilitated, 1 health center built and 4 water points installed and equipped. Traffic after project completion was higher than estimated at appraisal and travel time by vehicles was reduced by more than 85% through saving in travelling time by about 5 hours. The project has significantly reduced transport cost.

### Support to the Post-Conflict Reconstruction Programme for the Centre-North-West in Cote d'Ivoire.

The objective of the project is to increase access and improve the quality of urban infrastructure and services in roads, water and education in the four main cities in the CNO regions, Man, Bouake, Korhogo and Odionnc.

Because of the project, the water supply capacity to the city of Man increased from 4000 cubic meters per day to 15.000 cubic meters per day compared with a demand of 8.000 cubic meters a day. The road traffic has increased with an enhanced fluidity. At the technical school of Bouake which was temporarily located at Abidjan because of the negative aftermath of the armed conflict, enrolled more than doubled in Abidjan.

## 2.2 Some of the overall achievements

**Table 1 - Some additional progress towards the SDGs with SPDA**

SDG Goal	IsDB Core Sector Indicators
<b>Good Health</b> 	42 Health facilities constructed or upgraded or equipped 756 Health personnel trained 100 Number of beds added to health facilities) 725,100 Long Lasting Insecticidal Nets (LLINs) distributed 1,947,784 people reached through awareness campaigns
<b>Quality Education</b> 	1,224 additional persons accommodated in educational institutions 34 Residence rooms built or upgraded in hostels and accommodation in educational institutions 285 Classrooms built or upgraded in primary/secondary educational institutions 111 Institutions built or upgraded or equipped 70,500 Students benefitted 2,372 Teachers/Faculty/Staff trained
<b>Clean Energy</b> 	120 MW (Equivalent) of installed energy generation capacity using non-renewable sources 24,710 New households connected to electricity 913 KM of Transmission/Distribution lines installed, upgraded or rehabilitated 15,000 Households with access to potable water supply systems Increased potable water treatment capacity of 14,852 m3/day 45 Km of Sewerage network installed or upgraded 54 Km of Water supply network installed or upgraded
<b>Decent Work</b> 	578 Associations established or actively promoted 40 Market centers established, upgraded or rehabilitated 1929 People employed 7857 People trained 140,982 People accessing microfinance
<b>Infrastructure</b> 	1,2 million passengers of increased capacity at airports 510 KM of Expressways and National or Regional highways built, upgraded or rehabilitated 143 KM of Local/Rural roads built, upgraded or rehabilitated 1,560 KM of Fiber Optic Network laid

Source: Computed from OQR data

## VII Conclusion

23. The implementation of the SPDA projects is in its latest stage and has overall been satisfactory with very high number of completed operations, some active operations in their final stages and high degree of absorption with only US\$131 million still uncommitted, representing less than 5% of the gross OCR approvals. As mentioned above, of the completed operations, the largest number are in the form of grants amounting to USD 37 million, mainly for capacity building support to member countries which is consistent with IsDB's commitment to addressing the inadequate capacity that prevails in many of the SPDA countries. The grants average about USD 300,000. More than USD 41 million has so far been disbursed to support capacity development in the member countries.
24. The spotlight that was generated by the special programs appears to have significant traction and the high approvals continues even after the end of the approval phase of SPDA. In the 10 years following the end of the approval phase of the program, USD 9.6 Billion have been approved under OCR for the countries in the program, three times the amount of the program, despite the low approvals observed in the last 5 years. This is attributable to a large extent to the special programs such as SPDA and the Ouagadougou Declaration that have stimulated member countries appetite for IsDB financing. It is therefore reasonable to say that achieving high approvals is no longer a concern for the African countries and the focus now should be on two issues. Firstly, deepening the implementation of the active portfolio to ensure that the projects are completed on time and the expected outputs are delivered as intended. Secondly, ensuring that future IsDBG support to African member countries is anchored on a well-articulated regional strategy for Africa aiming at relaxing some of the most critical constraints facing the region in its quest to achieve sustainable development.
25. The implementation of SPDA is getting close to its end and with the decentralization exercise that the Bank has embarked upon, more projects are being completed and dormant projects are being closed. An analysis of project completion reports will be undertaken as soon as they are finalized to update the achievements of SPDA and give a more complete picture.

Annex 1: Active, Complete and Terminated IsDB Interventions under SPDA

Category	Active			Completed			Terminated			Count	Total Approvals (\$m)	Total Disbursements (\$m)
	Count	Approvals (\$m)	Disbursements (\$m)	Count	Approvals (\$m)	Disbursements (\$m)	Projects	Approvals (\$m)	Disbursements			
<b>Grant</b>	<b>1</b>	<b>5</b>	<b>4</b>	<b>123</b>	<b>37</b>	<b>37</b>				<b>124</b>	<b>42</b>	<b>42</b>
Agriculture	1	5	4	39	20	20				40	25	24
Education				12	3	3				12	3	3
Finance				19	6	6				19	6	6
Health & Social				46	7	7				46	7	7
ICT				1	0	0				1	0	0
Industry & Mining				1	0	0				1	0	0
Public Admin.				2	0	0				2	0	0
Transportation				1	0	0				1	0	0
Water & Urban S.				2	0	0				2	0	0
<b>Project</b>	<b>54</b>	<b>1,375</b>	<b>926</b>	<b>82</b>	<b>1,715</b>	<b>1,715</b>	<b>3</b>	<b>2</b>	<b>2</b>	<b>139</b>	<b>3,092</b>	<b>2,643</b>
Agriculture	25	643	379	15	274	274	2	1	1	42	918	654
Education	7	93	70	12	131	131				19	223	200
Energy	2	39	35	7	208	208				9	248	243
Finance	1	16	12	3	18	18				4	34	30
Health & Social	6	97	49	14	168	168	1	1	1	21	267	218
ICT				2	50	50				2	50	50
Industry & Mining	3	61	28	4	117	117				7	178	145
Transportation	5	252	225	16	595	595				21	847	819
Water & Urban S.	5	173	129	9	155	155				14	327	284
<b>Grand Total</b>	<b>55</b>	<b>1,380</b>	<b>931</b>	<b>205</b>	<b>1,753</b>	<b>1,753</b>	<b>3</b>	<b>2</b>	<b>2</b>	<b>263</b>	<b>3,134</b>	<b>2,685</b>

Annex 2: List of Approvals

Date of Approval	Country	Project	Sectors	Mode of Financing	Appr
2008-01-12	Gambia	Idd-Malaria Control Project - Quick Win Program	Health	Loan	3.00
2008-02-18	Senegal	Livestock Development Project In Eastern Senegal And Upper Casamance Region	Agriculture	Loan	10.34
2008-02-18	Sudan	Heightening Of Roseires Dam Project	Agriculture	Istisnaa	80.00
2008-02-18	Sudan	Heightening Of Roseires Dam Project	Agriculture	Istisnaa	11.20
2008-02-19	Mali	2nd Blindness Control Campaign	Health	Grant	0.06
2008-03-17	Somalia	Urgent Relief For Conflict & Drought Victims In South Of Somalia (1429).	Health	Other Grant	0.26
2008-03-19	Sudan	F.S. Of The Abu Hujar Private Investment Agriculture	Agriculture	Loan	0.16
2008-04-07	Guinea	Rehabilitation And Extension Of Conakry Electricity Distribution Grid Project	Energy	Loan	11.44
2008-04-13	Somalia	Livestock Development	Agriculture	Grant	0.33
2008-05-21	Mauritania	Quick Win Malaria Control	Health	Loan	3.10
2008-06-01	Sudan	Gezira University Upgrading And Development Project	Education	Loan	11.18
2008-06-01	Comoros	Provision Of Lab Equipment And Furniture For Four Secondary Schools In Comoros.	Education	Loan	0.20
2008-07-21	Mauritania	Drought Locust Striken Mauritania(Food Security)	Agriculture	Loan	2.00
2008-07-29	Benin	Replenishment Of Food Security Stocks-Phase I Jed Declaration	Agriculture	Grant	1.00
2008-07-29	Chad	Replenishment Of Food Security Stocks-Phase I Jed Declaration	Agriculture	Grant	0.50
2008-07-29	Comoros	Replenishment Of Food Security Stocks-Phase I Jed Declaration	Agriculture	Grant	0.50
2008-07-29	Djibouti	Replenishment Of Food Security Stocks-Phase I Jed Declaration.	Health	Grant	0.30
2008-07-29	Gambia	Replenishment Of Food Security Stocks-Phase I Jed Declaration	Agriculture	Grant	0.30
2008-07-29	Guinea Bissau	Replenishment Of Food Security Stocks-Phase I Jed Declaration	Agriculture	Grant	0.30
2008-07-29	Guinea	Replenishment Of Food Security Stocks-Phase I Jed Declaration	Agriculture	Grant	0.70
2008-07-29	Mauritania	Improving The Production Of Strategic Food Crop - Jeddah Declaration Phase 1	Agriculture	Grant	0.60
2008-07-29	Mali	Replenishment Of Food Security Stocks-Phase I Jed Declaration	Agriculture	Grant	1.50
2008-07-29	Mozambique	Replenishment Of Food Security Stocks-Phase I Jed Declaration	Agriculture	Grant	0.70
2008-07-29	Niger	Replenishment Of Food Security Stocks-Phase I Jed Declaration	Agriculture	Grant	1.65
2008-07-29	Senegal	Replenishment Of Food Security Stocks-Phase I Jed Declaration	Agriculture	Grant	1.25
2008-07-29	Sierra Leone	Replenishment Of Food Security Stocks-Phase I Jed Declaration	Agriculture	Grant	0.70
2008-07-29	Somalia	Replenishment Of Food Security Stocks-Phase I Jed Declaration	Agriculture	Grant	0.30
2008-07-29	Sudan	Replenishment Of Food Security Stocks-Phase I Jed Declaration	Agriculture	Grant	0.80



2008-07-29	Togo	Replenishment Of Food Security Stocks - Jed. Declaration (Phase 1)	Agriculture	Grant	0.70
2008-07-29	Burkina Faso	Replenishment Of Food Security Stocks-Phase I Jed Declaration	Agriculture	Grant	1.40
2008-08-24	Senegal	Upgrading Of Dakar Expressway	Transportation	Istisnaa	6.67
2008-08-24	Burkina Faso	Construction Of Koudougou-Dedougou Road Project	Transportation	Loan	16.30
2008-08-24	Sierra Leone	Construction Of Kenema-Pendembu Road Project	Transportation	Loan	12.43
2008-09-13	Burkina Faso	4th Blindness Control Campaign	Health	Grant	0.07
2008-09-17	Mauritania	Hydro-Agricultural Study Of R'kiz Buffer Zone	Agriculture	Grant	0.13
2008-10-27	Togo	Construction Of The Dapaong Ponio - Burkina Border Road	Transportation	Loan	9.28
2008-10-27	Gambia	Rural Water Supply Project In Gunjur	Water, San. & Urb. Ser.	Loan	4.74
2008-12-01	Gambia	2nd Phase Medical Relief And Health Training Program	Health	Grant	0.09
2008-12-03	Mali	Agro-Food Industry Forum	Agriculture	Grant	0.25
2008-12-03	Senegal	Action For Islamic Solidaritys Program For Integrated Manang.	Public Administration	Grant	0.10
2008-12-21	Chad	Arboutchatak-Bitkine Road Project	Transportation	Istisnaa	51.00
2008-12-21	Chad	Arboutchatak-Bitkine Road Project	Transportation	Loan	10.82
2008-12-21	Chad	Microfinance Project	Finance	Loan	6.40
2008-12-21	Cote D'ivoire	Support To The Post-Conflict Reconstruction Program For Center-North-West Zones	Water, San. & Urb. Ser.	Loan	10.00
2008-12-21	Cote D'ivoire	Support To The Post-Conflict Reconstruction Program For Center-North-West Zones	Water, San. & Urb. Ser.	Loan	10.00
2008-12-21	Cote D'ivoire	Support To The Post-Conflict Reconstruction Program For Center-North-West Zones	Water, San. & Urb. Ser.	Loan	9.40
2008-12-21	Burkina Faso	Dangoumana Hydro-Agricultural Development Project	Agriculture	Istisnaa	16.17
2008-12-21	Burkina Faso	Dangoumana Hydro-Agricultural Development Project	Agriculture	Loan	12.20
2008-12-21	Chad	Microfinance Project	Finance	Grant	0.30
2008-12-21	Cote D'ivoire	Support To The Post-Conflict Reconstruction Program For Center-North-West Zones	Water, San. & Urb. Ser.	Grant	0.37
2008-12-23	Sudan	C.B. For The Int'l Muslim Women Union	Education	Grant	0.16
2009-01-17	Sudan	The White Nile Sugar Project	Industry And Mining	Leasing	11.20
2009-01-30	Comoros	Health Sector Phase 2	Health	Grant	0.30
2009-02-08	Chad	Malaria Prevention Control Support (Quick Win)	Health	Grant	0.30

2009-02-08	Chad	Malaria Prevention Control Support (Quick Win)	Health	Loan	6.09
2009-03-15	Niger	5th Blindness Control Campaign	Health	Grant	0.07
2009-04-19	Burkina Faso	5th Blindness Control Campaign In Burkina Faso	Health	Grant	0.06
2009-05-12	Benin	3rd Blindness Control Campaign	Health	Grant	0.02
2009-05-17	Guinea	1st Blindness Control Campaign	Health	Grant	0.06
2009-05-31	Benin	Small Irrigated Perimeters Development Project (Jed. Declaration)	Agriculture	Loan	5.90
2009-05-31	Benin	Small Irrigated Perimeters Development Project (Jed. Declaration)	Agriculture	Istisnaa	8.84
2009-05-31	Togo	Construction Of Bassar-Katchamba Road Project	Transportation	Loan	11.61
2009-06-22	Benin	4th Blindness Control Campaign	Health	Grant	0.06
2009-06-22	Cameroon	2nd Blindness Control Campaign	Agriculture	Grant	0.07
2009-07-04	Mauritania	Guelb Ii Expansion Project (Tranche 1)	Industry And Mining	Leasing	80.00
2009-07-04	Mauritania	Snim - Railway Modernization Project	Transportation	Leasing	28.00
2009-07-04	Somalia	Design And Implement. Of Food Security (Jed. Declaration)	Agriculture	Grant	0.70
2009-07-04	Somalia	Medical Training Equipment And Material	Health	Grant	0.70
2009-07-08	Nigeria	Central Bank Of Nigeria (Cbn)	Finance	Grant	0.24
2009-07-12	Djibouti	Central Bank Of Djibouti To Devevelop A Regulatory And Supervisory Framework For Islamic Banking	Finance	Grant	0.07
2009-08-04	Guinea	Idb-Malaria Control Program - Quick Win Program	Health	Loan	8.12
2009-08-04	Guinea	Idb-Malaria Control Program - Quick Win Program	Health	Grant	0.30
2009-09-17	Burkina Faso	6th Blindness Control Campaign	Health	Grant	0.06
2009-10-04	Chad	2nd Blindness Control Campaign	Health	Grant	0.05
2009-10-17	Uganda	Construction Of A Girls' Hostel For The Islamic University In Uganda.	Education	Loan	0.35
2009-10-18	Burkina Faso	Construction And Equipping Of A Hostel For The Students Of The University Of Bobo-Dioulasso Project	Education	Loan	8.97
2009-10-18	Burkina Faso	Construction And Equipping Of A Hostel For The Students Of The University Of Bobo-Dioulasso Project	Education	Loan	3.12
2009-11-12	Cameroon	3rd Blindness Control Campaign	Health	Grant	0.06
2009-11-12	Mali	3rd Blindness Control Campaign	Health	Grant	0.08
2009-11-24	Burkina Faso	2nd Eye Care Caravan In Rural Area	Health	Grant	0.03
2009-12-21	Sudan	C.B. For Azza Women Associatio N (Awa)	Education	Grant	0.07
2009-12-27	Djibouti	Provision Of Veterinary Medicine And Feed (Jed. Declaration)	Agriculture	Grant	0.30

2009-12-27	Guinea	F.S. For Livestock Development Project (Jeddah Declaration)	Agriculture	Grant	0.50
2009-12-27	Mozambique	Provision Of Agricultural Inpu Ts (Jed. Declaration)	Agriculture	Grant	0.40
2009-12-27	Niger	Provision Of Agricultural Inpu Ts (Jed. Declaration)	Agriculture	Grant	0.40
2009-12-27	Sudan	Development Of Conservation Ag Riculture (Jed. Declaration)	Agriculture	Grant	0.50
2009-12-27	Uganda	F.S. For Agricultureal Project (Jed. Declaration)	Agriculture	Grant	0.50
2009-12-28	Niger	Eye Care Caravans In Rural Areas	Health	Grant	0.20
2010-01-04	Senegal	Ministry Of Economy Finance	Finance	Grant	0.31
2010-01-04	Nigeria	Holistic Approach To Eradicati Ng Obstetric Fistula	Health	Grant	0.10
2010-02-06	Sudan	Participation Financing For The Budget Of Darfur Donors Conference.	Finance	Loan	0.05
2010-02-20	Chad	3rd Blindness Control Campaign	Health	Grant	0.05
2010-03-13	Sierra Leone	Sierra Leone Community-Driven Development Project	Agriculture	Loan	8.43
2010-04-11	Burkina Faso	7th Blinness Control Campaign	Health	Grant	0.06
2010-04-16	Gambia	Obstetric Fistula Treatment Rehabilitation	Health	Grant	0.11
2010-05-02	Benin	5th 6th Blindness Control Campaigns	Health	Grant	0.06
2010-05-02	Cameroon	4th Blindness Control Campaign	Health	Grant	0.07
2010-05-09	Somalia	Relief Assistance For Drilling Water We	Finance	Other Grant	0.42
2010-05-12	Chad	4th Blindness Contorl Campaign	Health	Grant	0.07
2010-05-12	Mali	4th Blindness Control Campaign	Health	Grant	0.04
2010-06-12	Uganda	Construction Of Students Hostels In The Islamic University In Uganda Project	Education	Loan	0.97
2010-06-24	Senegal	Construction Of The Linguere-M Atam (Boula-Patouki) Road	Transportation	Istisnaa	14.21
2010-06-24	Senegal	Construction Of The Linguere-M Atam (Boula-Patouki) Road	Transportation	Loan	17.91
2010-06-24	Mali	F.S. Of The Development Of 2000 Ha In Diadian And Singo	Agriculture	Grant	0.30
2010-07-06	Senegal	Islamic Bank Of Senegal	Finance	Pr.Sh & Equity	4.43
2010-08-17	Sudan	Blindness Control Campaign	Health	Grant	0.08
2010-08-29	Niger	Monsoon Flooding Of 2010	Water, San. & Urb. Ser.	Grant	0.20
2010-09-06	Benin	C.B. For The Ministry Of Planning, Development, And Evaluation	Finance	Grant	0.30
2010-09-06	Chad	C.B. In Project Management Of General Directorate Of Ministry Of Economy And Planning	Finance	Grant	0.29
2010-09-11	Sudan	Training Program For Agri-Engineers (Ex. Health Services For Women And Children In South Sudan)	Health	Grant	0.10
2010-10-21	Uganda	C.B. Ws. On Coffee, Vanilla Poultry Farming For Women	Agriculture	Grant	0.09

2010-10-26	Uganda	Support Of Transfer Of Low-Cost Harcoal Manufacturing Technology To Farmers And Entrepreneurs	Industry And Mining	Grant	0.25
2010-10-27	Benin	Monsoon Flooding Of 2010	Water, San. & Urb. Ser.	Grant	0.20
2010-12-04	Niger	Islamic Bank Of Niger	Finance	Pr.Sh & Equity	3.93
2010-12-27	Gambia	Arab Gambian Islamic Bank (Agib) (Additional I)	Finance	Pr.Sh & Equity	0.70
2011-01-06	Mauritania	F.S. Of Tignend-Mederdra-Rkiz- Boutilimit Road	Transportation	Grant	0.30
2011-02-12	Mauritania	Scientific Education Of High Teacher Training College	Education	Grant	0.30
2011-03-22	Somalia	Idb Assistance To Drought Affected Inhabitants In Somalia	Health	Grant	0.20
2011-03-22	Somalia	Idb Assistance To Drought Affected Inhabitants In Somalia	Health	Grant	1.00
2011-03-28	Niger	Eye Care Caravans In Rural Areas	Health	Grant	0.18
2011-03-28	Burkina Faso	8th Blindness Control Program	Health	Grant	0.12
2011-04-13	Mozambique	Cotton Sector Revitalization Program In Mozambique	Agriculture	Grant	0.31
2011-05-01	Comoros	Ta Grant For Health Sector (Phase-Iii)	Health	Grant	0.44
2011-05-01	Comoros	C.B. In Budget Resilience And Absorptive Capacity	Finance	Grant	0.60
2011-05-04	Mali	Blindness Control Campaign	Health	Grant	0.05
2011-06-14	Senegal	Action For Islamic Solidarity's Program For The Integrated Management Of Childhood Illnesses	Health	Grant	0.06
2011-06-26	Mali	Basic Urban Infrastructure For A Social Housing Project In Bamako	Industry And Mining	Loan	10.67
2011-06-26	Mali	Basic Urban Infrastructure For A Social Housing Project In Bamako	Industry And Mining	Istisnaa	9.84
2011-07-19	Mozambique	Development Of Inland Artisanal Fisheries And Aquaculture	Agriculture	Grant	0.32
2011-07-25	Gambia	C.B. For Project Management	Public Administration	Grant	0.29
2011-08-15	Nigeria	Equipping And Modernizing The Science And Technology Laboratories At Crescent University	Education	Grant	0.30
2011-08-24	Sudan	Renewing The Patent Code To The Work For Production Of Sugar Cane	Finance	Grant	0.04
2011-10-23	Niger	Prevention Campaign On Breast Cancer Risks	Health	Grant	0.07
2011-10-24	Guinea Bissau	Institutional And Human Resource C.B. Of National Hospital Simao Mendes Project	Health	Grant	0.30
2012-02-19	Mali	Support To The Social Housing Program In Mali	Industry And Mining	Loan	6.46
2012-02-19	Mali	Support To The Social Housing Program In Mali	Industry And Mining	Istisnaa	6.15

2012-04-01	Chad	Emergency Assistance To Drought Affected Member Countries In Sahel Region	Agriculture	Grant	0.40
2012-04-01	Mauritania	Emergency Assistance To Drought Affected Member Countries In Sahel Region	Agriculture	Grant	0.40
2012-04-01	Mali	Emergency Assistance To Drought Affected Member Countries In Sahel Region	Agriculture	Grant	0.40
2012-04-01	Niger	Emergency Assistance To Drought Affected Member Countries In Sahel Region	Agriculture	Grant	0.40
2012-04-01	Burkina Faso	Emergency Assistance To Drought Affected Member Countries In Sahel Region	Agriculture	Grant	0.40
2012-04-09	Sudan	Participation In Equity Capital Of Al-Ebda'a Microfinance Institution In Sudan-Agfund	Finance	Pr.Sh & Equity	1.25
2012-05-13	Niger	Emergency Supporting Of Malian Refugees Flowing Into Niger	Health	Grant	0.10
2012-05-23	Nigeria	Study Visit Of Experts & Technicians On Dams And Irrigation Network	Finance	Grant	0.13
2012-07-14	Mali	Millennium Village Program (Mvp) Phase 2	Agriculture	Loan	2.00
2012-10-01	Burkina Faso	Blindness Control Program (2012)	Health	Grant	0.09

